



***New Protective Services Buildings
Construction Update
Mise à jour sur la Construction
des nouveaux bâtiments des
Services de la protection***

Caserne 1 – Bourget – Station 1

Caserne 3 – Rockland – Station 3



Bourget





Bourget

Juillet / July 2018





Bourget

Octobre / October 2018





Bourget

Novembre / November 2018





Bourget

Décembre / December 2018





Bourget

Janvier / January 2019





Bourget

Février / February 2019





Bourget

Mars / March 2019





Bourget

Avril / April 2019





Bourget

Avril / April 2019

Bourget Fire Station		3 Week Look Ahead Schedule																		
Activity \ Day	Day	Week of April 1st						Week of April 8th						Week of April 15th						FRI DAY
		M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	
Install Horizontal Siding Band																				
Install Accent Horizontal Siding																				G
Install Aluminum Doors & Caulk Windows																				O
Install U/G Plumbing																				D
Excavate & Install U/G Main Water																				F
Place & Compact Gran A																				R
Electrical Rough-In U/G for Panels etc...																				I
Pour Concrete Mezzanine Slab on Deck																				D
Install Large Ductwork in South End																				A
Install Wire Mesh , Pour SOG																				Y
Install Metal Studs for Walls																				H
Install Electrical Rough-In to Walls																				O
Install Plumbing into Walls																				L

Substantial Completion Date:

Baseline (Contract)

Current Projected

May 30, 2019

July 8, 2019



Bourget






Rockland





Rockland

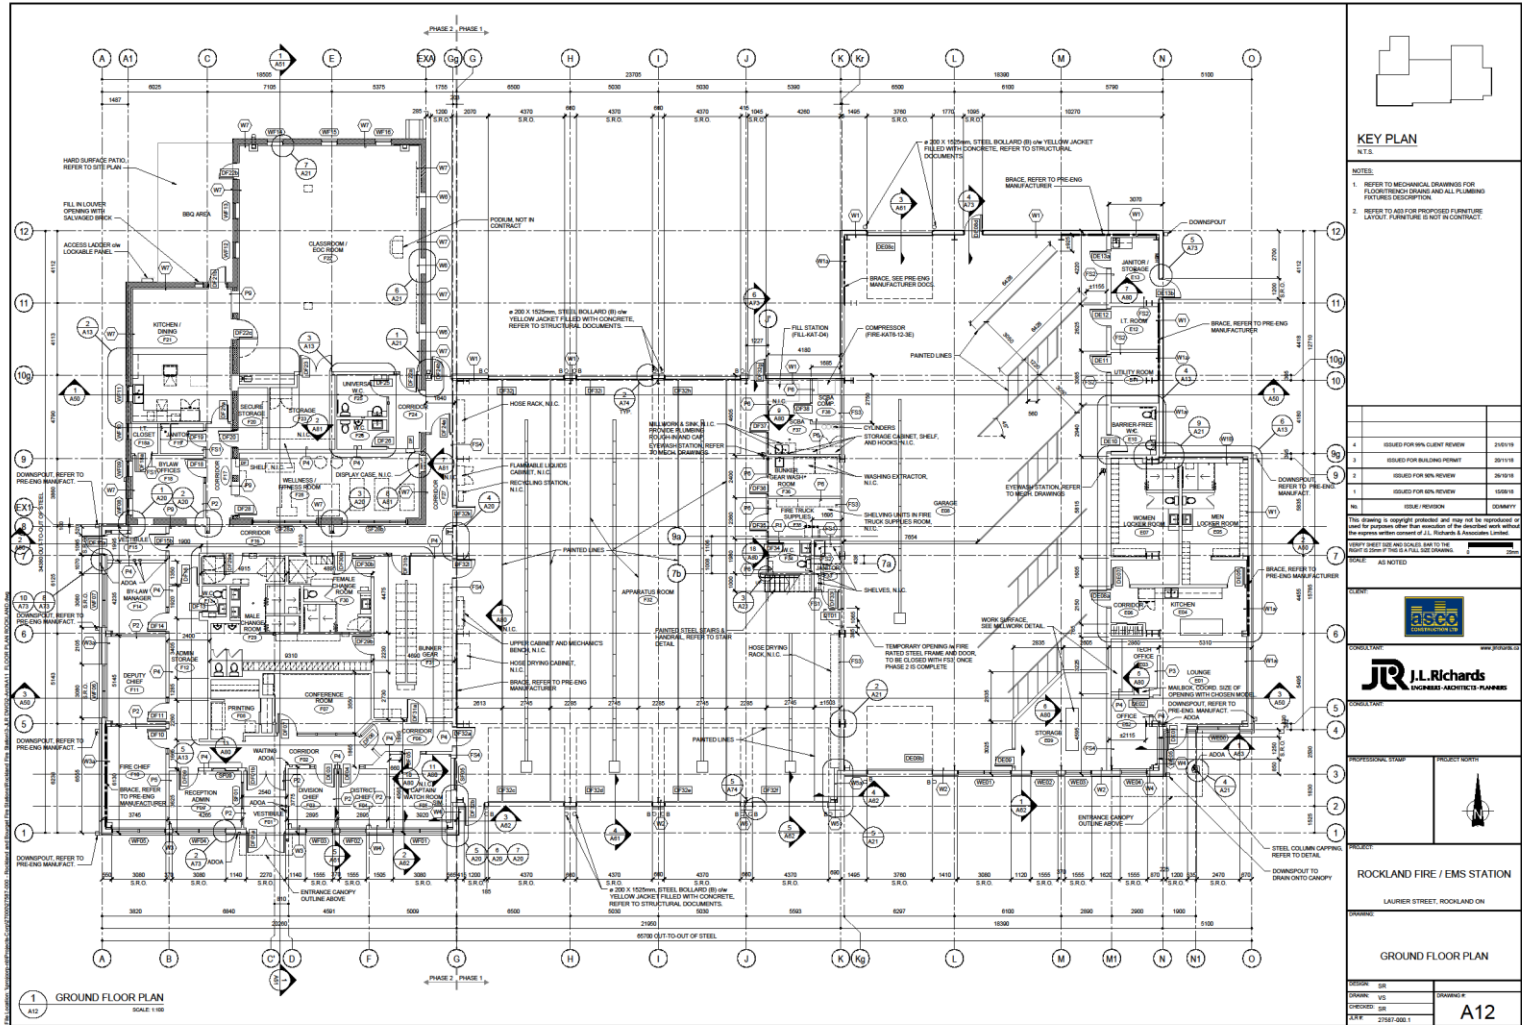



Rockland

Juillet / July 2018





Rockland

Octobre / October 2018





Rockland

Novembre / November 2018





Rockland

Décembre / December 2018





Rockland

Février / February 2019





Rockland Mars / March 2019





Rockland

Avril / April 2019





Rockland

Avril / April 2019

Rockland FS & EMS Station		3 Week Look Ahead Schedule																		
Activity \ Day	Day	Week of April 1st						Week of April 8th							Week of April 15th					
		M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
Ceiling liner																				
Wall liner & trims																				
Mezzanine Framing and Steel Deck																				
Mezzanine Slab on Deck																				
OH Doors Framing																				
HVAC																				
Electrical Rough in																				
Blueskin																				
Roof insulation and roofing																				
Wall exterior Siding																				
Blocking for signage																				
Framing of Metal stud wall Line G																				

Substantial Completion Date of Phase 1 (addition):

Baseline (Contract)

May 6, 2019

Current Projected

August 20, 2019

Substantial Completion Date of Phase 2 (final):

Baseline (Contract)

September 27, 2019

Current Projected

January 13, 2020



Rockland

